

Section 10,330**Statement of Position 81-1*
Accounting for Performance of
Construction-Type and Certain
Production-Type Contracts**

July 15, 1981

[Proposal to the Financial Accounting Standards Board]

Note: Statement of Position 81-1, *Accounting for Performance of Construction-Type and Certain Production-Type Contracts*, has been modified by the AICPA staff to include certain changes necessary due to the issuance of authoritative pronouncements since it was originally issued. The changes are identified in a schedule in Appendix D of the statement.

NOTE

Statements of Position of the Accounting Standards Division present the conclusions of at least a majority of the Accounting Standards Executive Committee, which is the senior technical body of the AICPA authorized to speak for the Institute in the areas of financial accounting and reporting. Statement on Auditing Standards No. 69, *The Meaning of Present Fairly in Conformity With Generally Accepted Accounting Principles*, identifies AICPA Statements of Position as sources of established accounting principles that an AICPA member should consider if the accounting treatment of a transaction or event is not specified by a pronouncement covered by Rule 203 of the AICPA Code of Professional Conduct. In such circumstances, the accounting treatment specified by this Statement of Position should be used or the member should be prepared to justify a conclusion that another treatment better presents the substance of the transaction in the circumstances. However, an entity need not change an accounting treatment followed as of March 15, 1992 to the accounting treatment specified in this Statement of Position.

Introduction

.01 This statement of position provides guidance on the application of generally accepted accounting principles in accounting for the performance of contracts for which specifications are provided by the customer for the construction of facilities or the production of goods or for the provision of related services. Changes in the business environment have increased significantly the variety and uses of those types of contracts and the types of business enterprises that use them. In the present business environment, diverse types of contracts, ranging from relatively simple to highly complex and from relatively short- to long-term, are widely used in many industries for construction, production, or provision of a broad range of goods and services. However, existing principles related to accounting for contracts were written in terms of long-term construction-type contracts, and they are not stated in sufficient detail for the scope of activities

* Transactions within the scope of SOP 81-1 are not subject to the views expressed in Staff Accounting Bulletin (SAB) 101, *Revenue Recognition in Financial Statements*, issued by the Securities and Exchange Commission.

to which they presently are applied. Those activities range far beyond the traditional construction-type activity (the design and physical construction of facilities such as buildings, roads, dams, and bridges) to include, for example, the development and production of military and commercial aircraft, weapons delivery systems, space exploration hardware, and computer software. The accounting standards division believes that guidance is now needed in this area of accounting.

The Basic Accounting Issue

.02 The determination of the point or points at which revenue should be recognized as earned and costs should be recognized as expenses is a major accounting issue common to all business enterprises engaged in the performance of contracts of the types covered by this statement. Accounting for such contracts is essentially a process of measuring the results of relatively long-term events and allocating those results to relatively short-term accounting periods. This involves considerable use of estimates in determining revenues, costs, and profits and in assigning the amounts to accounting periods. The process is complicated by the need to evaluate continually the uncertainties inherent in the performance of contracts and by the need to rely on estimates of revenues, costs, and the extent of progress toward completion.

Present Accounting Requirements and Practices

.03 The pervasive principle of realization and its exceptions and modifications are central factors underlying accounting for contracts. APB Statement 4[†] states:

Revenue is generally recognized when both of the following conditions are met: (1) the earnings process is complete or virtually complete, and (2) an exchange has taken place. [Paragraph 150]

Revenue is sometimes recognized on bases other than the realization rule. For example, on long-term construction contracts revenue may be recognized as construction progresses. This exception to the realization principle is based on the availability of evidence of the ultimate proceeds and the consensus that a better measure of periodic income results. [Paragraph 152]

The exception to the usual revenue realization rule for long-term construction-type contracts, for example, is justified in part because strict adherence to realization at the time of sale would produce results that are considered to be unreasonable. The judgment of the profession is that revenue should be recognized in this situation as construction progresses. [Paragraph 174]

.04 Accounting Research Bulletin No. 45 (ARB No. 45), *Long-Term Construction-Type Contracts*, issued by the AICPA Committee on Accounting Procedure in 1955, describes the two generally accepted methods of accounting for long-term construction-type contracts for financial reporting purposes:

- *The percentage-of-completion method* recognizes income as work on a contract progresses; recognition of revenues and profits generally is related to costs incurred in providing the services required under the contract.
- *The completed-contract method* recognizes income only when the contract is completed, or substantially so, and all costs and related revenues are reported as deferred items in the balance sheet until that time.

[†] Statement of Position 93-3, *Rescission of Accounting Principles Board Statements*, rescinds APB Statement No. 4, FASB Concepts Statement No. 5, *Recognition and Measurement in Financial Statements of Business Enterprises*, discusses matters similar to those in APB Statement No. 4. [Footnote added, April 1996, to reflect conforming changes necessary due to the issuance of recent authoritative literature.]

The units-of-delivery is a modification of the percentage-of-completion method of accounting for contracts.

- *The units-of-delivery method* recognizes as revenue the contract price of units of a basic production product delivered during a period and as the cost of earned revenue the costs allocable to the delivered units; costs allocable to undelivered units are reported in the balance sheet as inventory or work in progress. The method is used in circumstances in which an entity produces units of a basic product under production-type contracts in a continuous or sequential production process to buyers' specifications.

The use of either of the two generally accepted methods of accounting involves, to a greater or lesser extent, three key areas of estimates and uncertainties: (a) the extent of progress toward completion, (b) contract revenues, and (c) contract costs. Although the ultimate amount of contract revenue is often subject to numerous uncertainties, the accounting literature has given little attention to the difficulties of estimating contract revenue. [Revised, April 1996, to reflect conforming changes necessary due to the issuance of recent authoritative literature.]

.05 ARB No. 45, paragraph 15, describes the circumstances in which each method is preferable as follows:

The committee believes that in general when estimates of costs to complete and extent of progress toward completion of long-term contracts are reasonably dependable, the percentage-of-completion method is preferable. When lack of dependable estimates or inherent hazards cause forecasts to be doubtful, the completed-contract method is preferable.

Both of the two generally accepted methods are widely used in practice. However, the two methods are frequently applied differently in similar circumstances. The division believes that the two methods should be used in specified circumstances and should not be used as acceptable alternatives for the same circumstances. Accordingly, identifying the circumstances in which either of the methods is preferable and the accounting that should be followed in the application of those methods are among the primary objectives of this statement of position. This statement provides guidance on the application of ARB No. 45 and does not amend that bulletin.

.06 In practice, methods are sometimes found that allocate contract costs and revenues to accounting periods on (a) the basis of cash receipts and payments or (b) the basis of contract billings and costs incurred. Those practices are not generally accepted methods of accounting for financial reporting purposes. However, those methods are appropriate for other purposes, such as the measurement of income for income tax purposes, for which the timing of cash transactions is a controlling factor. Recording the amounts billed or billable on a contract during a period as contract revenue of the period, and the costs incurred on the contract as expenses of the period, is not acceptable for financial reporting purposes because the amounts billed or billable on a contract during a period are determined by contract terms and do not necessarily measure performance on the contract. Only by coincidence might those unacceptable methods produce results that approximate the results of the generally accepted method of accounting for contracts that are appropriate in the circumstances.

Other Pronouncements and Regulations Affecting Contract Accounting

.07 Accounting Research Bulletin No. 43, chapter 11, "Government Contracts," prescribes generally accepted principles in three areas of accounting

for government contracts. Section A of that chapter deals with accounting problems arising under cost-plus-fixed-fee contracts. Section B deals with certain aspects of the accounting for government contracts and subcontracts that are subject to renegotiation. Section C deals with problems involved in accounting for certain terminated war and defense contracts. Those pronouncements govern accounting for contracts in the areas indicated.

.08 The pricing and costing of federal government contracts are governed by cost principles contained in procurement regulations such as the Federal Procurement Regulation (FPR) and the Defense Acquisition Regulation (DAR). Also, most major government contractors are subject to cost accounting standards issued by the Cost Accounting Standards Board (CASB). CASB standards apply to the cost accounting procedures that government contractors use to allocate costs to contracts; CASB standards are not intended for financial reporting.

.09 Accounting for contracts for income tax purposes is prescribed by the Internal Revenue Code and the related rules and regulations. The methods of accounting for contracts under those requirements are not limited to the two generally accepted methods for financial reporting. For numerous historical and practical reasons, tax accounting rules and regulations differ from generally accepted accounting principles. Numerous nonaccounting considerations are appropriate in determining income tax accounting. This statement deals exclusively with the application of generally accepted accounting principles to accounting for contracts in financial reporting. It does not apply to income tax accounting and is not intended to influence income tax accounting.

Need for Guidance

.10 Because of the complexities and uncertainties in accounting for contracts, the increased use of diverse types of contracts for the construction of facilities, the production of goods, or the provision of related services, and present conditions and practices in industries in which contracts are performed for those purposes, additional guidance on the application of generally accepted accounting principles is needed. This statement of position provides that guidance. Appendix A contains a schematic chart showing the organization of the statement.

Scope of Statement of Position

.11 This statement of position applies to accounting for performance of contracts for which specifications are provided by the customer for the construction of facilities or the production of goods or the provision of related services that are reported in financial statements prepared in conformity with generally accepted accounting principles.¹ Existing authoritative accounting literature uses the terms “long-term” and “construction-type” in identifying the types of contracts that are the primary focus of interest. The term “long-term” is not used in this statement of position as an identifying characteristic because

¹ This statement is not intended to apply to “service transactions” as defined in the FASB’s October 23, 1978 Invitation to Comment, *Accounting for Certain Service Transactions*. However, it applies to separate contracts to provide services essential to the construction or production of tangible property, such as design, engineering, procurement, and construction management (see paragraph .13 for examples).

other characteristics are considered more relevant for identifying the types of contracts covered. However, accounting for contracts by an entity that primarily has relatively short-term contracts is recommended in paragraph .31 of this statement. The scope of the statement is not limited to construction-type contracts.

Contracts Covered

.12 Contracts covered by this statement of position are binding agreements between buyers and sellers in which the seller agrees, for compensation, to perform a service to the buyer's specifications.² Contracts consist of legally enforceable agreements in any form and include amendments, revisions, and extensions of such agreements. Performance will often extend over long periods, and the seller's right to receive payment depends on his performance in accordance with the agreement. The service may consist of designing, engineering, fabricating, constructing, or manufacturing related to the construction or the production of tangible assets. Contracts such as leases and real estate agreements, for which authoritative accounting literature provides special methods of accounting, are not covered by this statement.

.13 Contracts covered by this statement include, but are not limited to, the following:

- Contracts in the construction industry, such as those of general building, heavy earth moving, dredging, demolition, design-build contractors, and specialty contractors (for example, mechanical, electrical, or paving).
- Contracts to design and build ships and transport vessels.
- Contracts to design, develop, manufacture, or modify complex aerospace or electronic equipment to a buyer's specification or to provide services related to the performance of such contracts.
- Contracts for construction consulting service, such as under agency contracts or construction management agreements.
- Contracts for services performed by architects, engineers, or architectural or engineering design firms.

.14 Contracts not covered by this statement include, but are not limited to, the following:

- Sales by a manufacturer of goods produced in a standard manufacturing operation, even if produced to buyers' specifications, and sold in the ordinary course of business through the manufacturer's regular marketing channels if such sales are normally recognized as revenue in accordance with the realization principle for sales of products and if their costs are accounted for in accordance with generally accepted principles of inventory costing.
- Sales or supply contracts to provide goods from inventory or from homogeneous continuing production over a period of time.
- Contracts included in a program and accounted for under the program method of accounting. For accounting purposes, a program consists of

² Specifications imposed on the buyer by a third party (for example, a government or regulatory agency or a financial institution) or by conditions in the marketplace are deemed to be "buyer's specifications."

a specified number of units of a basic product expected to be produced over a long period in a continuing production effort under a series of existing and anticipated contracts.³

- Service contracts of health clubs, correspondence schools, and similar consumer-oriented organizations that provide their services to their clients over an extended period.
- Magazine subscriptions.
- Contracts of nonprofit organizations to provide benefits to their members over a period of time in return for membership dues.

.15 Contracts covered by this statement may be classified into four broad types based on methods of pricing: (a) fixed-price or lump-sum contracts, (b) cost-type (including cost-plus) contracts, (c) time-and-material contracts, and (d) unit-price contracts. A fixed-price contract is an agreement to perform all acts under the contract for a stated price. A cost-type contract is an agreement to perform under a contract for a price determined on the basis of a defined relationship to the costs to be incurred, for example, the costs of all acts required plus a fee, which may be a fixed amount or a fixed percentage of the costs incurred. A time-and-material contract is an agreement to perform all acts required under the contract for a price based on fixed hourly rates for some measure of the labor hours required (for example, direct labor hours) and the cost of materials. A unit-price contract is an agreement to perform all acts required under the contract for a specified price for each unit of output. Each of the various types of contracts may have incentive, penalty, or other provisions that modify their basic pricing terms. The pricing features of the various types are discussed in greater detail in Appendix B.

Definition of a Contractor

.16 The term “contractor” as used in this statement refers to a person or entity that enters into a contract to construct facilities, produce goods, or render services to the specifications of a buyer either as a general or prime contractor, as a subcontractor to a general contractor, or as a construction manager.

Definition of a Profit Center

.17 For the purpose of this statement, a “profit center” is the unit for the accumulation of revenues and costs and the measurement of income. For business enterprises engaged in the performance of contracts, the profit center for accounting purposes is usually a single contract; but under some specified circumstances it may be a combination of two or more contracts, a segment of a contract or of a group of combined contracts. This statement of position provides guidance on the selection of the appropriate profit center. The accounting recommendations, usually stated in terms of a single contract, also apply to alternative profit centers in circumstances in which alternative centers are appropriate.

Application and Effect on Existing Audit Guides and SOPs

.18 This statement of position presents the division’s recommendations on accounting for contracts (as specified in paragraphs .11 to .17) in all indus-

³ [Footnote deleted, April 1996, to reflect conforming changes necessary due to the issuance of recent authoritative literature.]

tries. The recommendations in this statement need not be applied to immaterial items. Two existing AICPA Audit and Accounting Guides, *Construction Contractors* and *Federal Government Contractors*, provide additional guidance on the application of generally accepted accounting principles to the construction industry and to federal government contracts, respectively. The recommendations in this statement take precedence in those areas. [Revised, April 1996, to reflect conforming changes necessary due to the issuance of recent authoritative literature.]

.19 The guidance on contract accounting and financial reporting in *Federal Government Contractors* is essentially consistent with the recommendations in this statement. Since the recommendations in this statement provide more comprehensive and explicit guidance on the application of generally accepted accounting principles to contract accounting than does the guide, *Federal Government Contractors*, the guide incorporates this statement as an appendix. The provisions of that guide should be interpreted and applied in the context of the recommendations in this statement. [Revised, April 1996, to reflect conforming changes necessary due to the issuance of recent authoritative literature.]

.20 This statement is not intended to supersede recommendations on accounting in other AICPA industry accounting or audit guides or in other statements of position.

The Division's Conclusions

Determining a Basic Accounting Policy for Contracts

.21 In accounting for contracts, the basic accounting policy decision is the choice between the two generally accepted methods: the percentage-of-completion method including units of delivery and the completed-contract method. The determination of which of the two methods is preferable should be based on a careful evaluation of circumstances because the two methods should not be acceptable alternatives for the same circumstances. The division's recommendations on basic accounting policy are set forth in the sections on "The Percentage-of-Completion Method" and "The Completed-Contract Method," which identify the circumstances appropriate to the methods, the bases of applying the methods, and the reasons for the recommendations. The recommendations apply to accounting for individual contracts and to accounting for other profit centers in accordance with the recommendations in the section on "Determining the Profit Center." As a result of evaluating individual contracts and profit centers, a contractor should be able to establish a basic policy that should be followed in accounting for most of his contracts. In accordance with the requirements of APB Opinion No. 22, *Disclosure of Accounting Policies*, a contractor should disclose in the note to the financial statements on accounting policies the method or methods of determining earned revenue and the cost of earned revenue including the policies relating to combining and segmenting, if applicable. Appendix C contains a summary of the disclosure requirements in this statement.

The Percentage-of-Completion Method

.22 This section sets forth the recommended basis for using the percentage-of-completion method and the reasons for the recommendation. Under most

contracts for construction of facilities, production of goods, or provision of related services to a buyer's specifications, both the buyer and the seller (contractor) obtain enforceable rights. The legal right of the buyer to require specific performance of the contract means that the contractor has, in effect, agreed to sell his rights to work-in-progress as the work progresses. This view is consistent with the contractor's legal rights; he typically has no ownership claim to the work-in-progress but has lien rights. Furthermore, the contractor has the right to require the buyer, under most financing arrangements, to make progress payments to support his ownership investment and to approve the facilities constructed (or goods produced or services performed) to date if they meet the contract requirements. The buyer's right to take over the work-in-progress at his option (usually with a penalty) provides additional evidence to support that view. Accordingly, the business activity taking place supports the concept that in an economic sense performance is, in effect, a continuous sale (transfer of ownership rights) that occurs as the work progresses. Also under most contracts for the production of goods and the provision of related services that are accounted for on the basis of units delivered, both the contractor and the customer obtain enforceable rights as the goods are produced or the services are performed. As units are delivered, title to and the risk of loss on those units normally transfer to the customer, whose acceptance of the items indicates that they meet the contractual specifications. For such contracts, delivery and acceptance are objective measurements of the extent to which the contracts have been performed. The percentage-of-completion method recognizes the legal and economic results of contract performance on a timely basis. Financial statements based on the percentage-of-completion method present the economic substance of a company's transactions and events more clearly and more timely than financial statements based on the completed-contract method, and they present more accurately the relationships between gross profit from contracts and related period costs. The percentage-of-completion method informs the users of the general purpose financial statements of the volume of economic activity of a company.

Circumstances Appropriate to the Method

.23 The use of the percentage-of-completion method depends on the ability to make reasonably dependable estimates. For the purposes of this statement, "the ability to make reasonably dependable estimates" relates to estimates of the extent of progress toward completion, contract revenues, and contract costs. The division believes that the percentage-of-completion method is preferable as an accounting policy in circumstances in which reasonably dependable estimates can be made and in which all the following conditions exist:

- Contracts executed by the parties normally include provisions that clearly specify the enforceable rights regarding goods or services to be provided and received by the parties, the consideration to be exchanged, and the manner and terms of settlement.
- The buyer can be expected to satisfy his obligations under the contract.
- The contractor can be expected to perform his contractual obligations.

.24 For entities engaged on a continuing basis in the production and delivery of goods or services under contractual arrangements and for whom contracting represents a significant part of their operations, the presumption is that they have the ability to make estimates that are sufficiently dependable

to justify the use of the percentage-of-completion method of accounting.⁴ Persuasive evidence to the contrary is necessary to overcome that presumption. The ability to produce reasonably dependable estimates is an essential element of the contracting business. For a contract on which a loss is anticipated, generally accepted accounting principles require recognition of the entire anticipated loss as soon as the loss becomes evident. An entity without the ability to update and revise estimates continually with a degree of confidence could not meet that essential requirement of generally accepted accounting principles.

.25 Accordingly, the division believes that entities with significant contracting operations generally have the ability to produce reasonably dependable estimates and that for such entities the percentage-of-completion method of accounting is preferable in most circumstances. The method should be applied to individual contracts or profit centers, as appropriate.

- a. Normally, a contractor will be able to estimate total contract revenue and total contract cost in single amounts. Those amounts should normally be used as the basis for accounting for contracts under the percentage-of-completion method.
- b. For some contracts, on which some level of profit is assured, a contractor may only be able to estimate total contract revenue and total contract cost in ranges of amounts. If, based on the information arising in estimating the ranges of amounts and all other pertinent data, the contractor can determine the amounts in the ranges that are most likely to occur, those amounts should be used in accounting for the contract under the percentage-of-completion method. If the most likely amounts cannot be determined, the lowest probable level of profit in the range should be used in accounting for the contract until the results can be estimated more precisely.
- c. However, in some circumstances, estimating the final outcome may be impractical except to assure that no loss will be incurred. In those circumstances, a contractor should use a zero estimate of profit; equal amounts of revenue and cost should be recognized until results can be estimated more precisely. A contractor should use this basis only if the bases in (a) or (b) are clearly not appropriate. A change from a zero estimate of profit to a more precise estimate should be accounted for as a change in an accounting estimate.

An entity using the percentage-of-completion method as its basic accounting policy should use the completed-contract method for a single contract or a group of contracts for which reasonably dependable estimates cannot be made or for which inherent hazards make estimates doubtful. Such a departure from the basic policy should be disclosed.

Nature of Reasonable Estimates and Inherent Hazards

.26 In practice, contract revenues and costs are estimated in a wide variety of ways ranging from rudimentary procedures to complex methods and

⁴ The division recognizes that many contractors have informal estimating procedures that may result in poorly documented estimates and marginal quality field reporting and job costing systems. Those conditions may influence the ability of an entity to produce reasonably dependable estimates. However, procedures and systems should not influence the development of accounting principles and should be dealt with by management as internal control, financial reporting, and auditing concerns.

systems. Regardless of the techniques used, a contractor's estimating procedures should provide reasonable assurance of a continuing ability to produce reasonably dependable estimates.⁵ Ability to estimate covers more than the estimating and documentation of contract revenues and costs; it covers a contractor's entire contract administration and management control system. The ability to produce reasonably dependable estimates depends on all the procedures and personnel that provide financial or production information on the status of contracts. It encompasses systems and personnel not only of the accounting department but of all areas of the company that participate in production control, cost control, administrative control, or accountability for contracts. Previous reliability of a contractor's estimating process is usually an indication of continuing reliability, particularly if the present circumstances are similar to those that prevailed in the past.

.27 Estimating is an integral part of contractors' business activities, and there is a necessity to revise estimates on contracts continually as the work progresses. The fact that circumstances may necessitate frequent revision of estimates does not indicate that the estimates are unreliable for the purpose for which they are used. Although results may differ widely from original estimates because of the nature of the business, the contractor, in the conduct of his business, may still find the estimates reasonably dependable. Despite these widely recognized conditions, a contractor's estimates of total contract revenue and total contract costs should be regarded as reasonably dependable if the minimum total revenue and the maximum total cost can be estimated with a sufficient degree of confidence to justify the contractor's bids on contracts.

.28 ARB No. 45 discourages the use of the percentage-of-completion method of accounting in circumstances in which inherent hazards make estimates doubtful. "Inherent hazards" relate to contract conditions or external factors that raise questions about contract estimates and about the ability of either the contractor or the customer to perform his obligations under the contract. Inherent hazards that may cause contract estimates to be doubtful usually differ from inherent business risks. Business enterprises engaged in contracting, like all business enterprises, are exposed to numerous business risks that vary from contract to contract. The reliability of the estimating process in contract accounting does not depend on the absence of such risks. Assessing business risks is a function of users of financial statements.

.29 The present business environment and the refinement of the estimating process have produced conditions under which most business entities engaged in contracting can deal adequately with the normal, recurring business risks in estimating the outcome of contracts. The division believes that inherent hazards that make otherwise reasonably dependable contract estimates doubtful involve events and conditions that would not be considered in the ordinary preparation of contract estimates and that would not be expected to recur frequently, given the contractor's normal business environment. Such hazards are unrelated to, or only incidentally related to, the contractor's typical activities. Such hazards may relate, for example, to contracts whose validity is seriously in question (that is, which are less than fully enforceable), to contracts whose completion may be subject to the outcome of pending legislation

⁵ The type of estimating procedures appropriate in a particular set of circumstances depends on a careful evaluation of the costs and benefits of developing the procedures. The ability to produce reasonably dependable estimates that would justify the use of the percentage-of-completion method as recommended in paragraph .25 does not depend on the elaborateness of the estimating procedures used.

or pending litigation, or to contracts exposed to the possibility of the condemnation or expropriation of the resulting properties. Reasonably dependable estimates cannot be produced for a contract with unrealistic or ill-defined terms or for a contract between unreliable parties. However, the conditions stated in paragraph .23 for the use of the percentage-of-completion method of accounting, which apply to most bona fide contracts, make the existence of some uncertainties, including some of the type described in ARB No. 45, paragraph 15, unlikely for contracts that meet those conditions. Therefore, the division believes that there should be specific, persuasive evidence of such hazards to indicate that use of the percentage-of-completion method on one of the bases in paragraph .25 is not preferable.

The Completed-Contract Method

.30 This section sets forth the recommended basis for using the completed-contract method and the reasons for the recommendation. Under the completed-contract method, income is recognized only when a contract is completed or substantially completed. During the period of performance, billings and costs are accumulated on the balance sheet, but no profit or income is recorded before completion or substantial completion of the work. This method precludes reporting on the performance that is occurring under the enforceable rights of the contract as work progresses. Although the completed-contract method is based on results as finally determined rather than on estimates for unperformed work, which may involve unforeseen costs and possible losses, it does not reflect current performance when the period of a contract extends beyond one accounting period, and it therefore may result in irregular recognition of income. Financial statements based on this method may not show informative relationships between gross profit reported on contracts and related period costs.

Circumstances of Use

.31 The completed-contract method may be used as an entity's basic accounting policy in circumstances in which financial position and results of operations would not vary materially from those resulting from use of the percentage-of-completion method (for example, in circumstances in which an entity has primarily short-term contracts). Although this statement does not formally distinguish on the basis of length between long-term and short-term contracts, the basis for recording income on contracts of short duration poses relatively few problems. In accounting for such contracts, income ordinarily is recognized when performance is substantially completed and accepted. Under those circumstances, revenues and costs in the aggregate for all contracts would be expected to result in a matching of gross profit with period overhead or fixed costs similar to that achieved by use of the percentage-of-completion method. For example, the completed-contract method, as opposed to the percentage-of-completion method, would not usually produce a material difference in net income or financial position for a small plumbing contractor that performs primarily relatively short-term contracts during an accounting period; performance covers such a short span of time that the work is somewhat analogous to the manufacture of shelf production items for sale. An entity using the completed-contract method as its basic accounting policy should depart from that policy for a single contract or a group of contracts not having the features described in this paragraph and use the percentage-of-completion method on one of the bases described in paragraph .25. Such a departure should be disclosed.

.32 The completed-contract method is preferable in circumstances in which estimates cannot meet the criteria for reasonable dependability discussed in the section on the percentage-of-completion method or in which there are inherent hazards of the nature of those discussed in that section. An entity using the percentage-of-completion method as its basic accounting policy should depart from that policy and use the completed-contract method for a single contract or a group of contracts only in the circumstances described in paragraph .25.

.33 The use of the completed-contract method is recommended for the circumstances described in paragraphs .31 and .32. However, for circumstances in which there is an assurance that no loss will be incurred on a contract (for example, when the scope of the contract is ill-defined but the contractor is protected by a cost-plus contract or other contractual terms), the percentage-of-completion method based on a zero profit margin, rather than the completed-contract method, is recommended until more precise estimates can be made. The significant difference between the percentage-of-completion method applied on the basis of a zero profit margin and the completed-contract method relates to the effects on the income statement. Under the zero profit margin approach to applying the percentage-of-completion method, equal amounts of revenue and cost, measured on the basis of performance during the period, are presented in the income statement; whereas, under the completed-contract method, performance for a period is not reflected in the income statement, and no amount is presented in the income statement until the contract is completed. The zero profit margin approach to applying the percentage-of-completion method gives users of general purpose financial statements an indication of the volume of a company's business and of the application of its economic resources.

Determining the Profit Center

.34 The basic presumption should be that each contract is the profit center for revenue recognition, cost accumulation, and income measurement. That presumption may be overcome only if a contract or a series of contracts meets the conditions described for combining or segmenting contracts. A group of contracts (combining), and a phase or segment of a single contract or of a group of contracts (segmenting) may be used as a profit center in some circumstances. Since there are numerous practical implications of combining and segmenting contracts, evaluation of the circumstances, contract terms, and management intent are essential in determining contracts that may be accounted for on those bases.

Combining Contracts

.35 A group of contracts may be so closely related that they are, in effect, parts of a single project with an overall profit margin, and accounting for the contracts individually may not be feasible or appropriate. Under those circumstances, consideration should be given to combining such contracts for profit recognition purposes. The presumption in combining contracts is that revenue and profit are earned, and should be reported, uniformly over the performance of the combined contracts. For example, a group of construction-type contracts may be negotiated as a package with the objective of achieving an overall profit margin, although the profit margins on the individual contracts may vary. In those circumstances, if the individual contracts are performed and reported in different periods and accounted for separately, the reported profit margins in those periods will differ from the profit margin contemplated in the negotiations for reasons other than differences in performance.

.36 Contracts may be combined for accounting purposes only if they meet the criteria in paragraphs .37 and .38.

.37 A group of contracts may be combined for accounting purposes if the contracts

- a.* Are negotiated as a package in the same economic environment with an overall profit margin objective. Contracts not executed at the same time may be considered to have been negotiated as a package in the same economic environment only if the time period between the commitments of the parties to the individual contracts is reasonably short. The longer the period between the commitments of the parties to the contracts, the more likely it is that the economic circumstances affecting the negotiations have changed.
- b.* Constitute in essence an agreement to do a single project. A project for this purpose consists of construction, or related service activity with different elements, phases, or units of output that are closely interrelated or interdependent in terms of their design, technology, and function or their ultimate purpose or use.
- c.* Require closely interrelated construction activities with substantial common costs that cannot be separately identified with, or reasonably allocated to, the elements, phases, or units of output.
- d.* Are performed concurrently or in a continuous sequence under the same project management at the same location or at different locations in the same general vicinity.
- e.* Constitute in substance an agreement with a single customer. In assessing whether the contracts meet this criterion, the facts and circumstances relating to the other criteria should be considered. In some circumstances different divisions of the same entity would not constitute a single customer if, for example, the negotiations are conducted independently with the different divisions. On the other hand, two or more parties may constitute in substance a single customer if, for example, the negotiations are conducted jointly with the parties to do what in essence is a single project.

Contracts that meet all of these criteria may be combined for profit recognition and for determining the need for a provision for losses in accordance with ARB No. 45, paragraph 6. The criteria should be applied consistently to contracts with similar characteristics in similar circumstances.

.38 Production-type contracts that do not meet the criteria in paragraph .37 or segments of such contracts may be combined into groupings such as production lots or releases for the purpose of accumulating and allocating production costs to units produced or delivered on the basis of average unit costs in the following circumstances:^[6]

- a.* The contracts are with one or more customers for the production of substantially identical units of a basic item produced concurrently or sequentially.
- b.* Revenue on the contracts is recognized on the units-of-delivery basis of applying the percentage-of-completion method.

^[6] [Footnote deleted to reflect the conforming changes necessary due to the issuance of recent authoritative literature.]

Segmenting a Contract

.39 A single contract or a group of contracts that otherwise meet the test for combining may include several elements or phases, each of which the contractor negotiated separately with the same customer and agreed to perform without regard to the performance of the others. If those activities are accounted for as a single profit center, the reported income may differ from that contemplated in the negotiations for reasons other than differences in performance. If the project is segmented, revenues can be assigned to the different elements or phases to achieve different rates of profitability based on the relative value of each element or phase to the estimated total contract revenue. A project, which may consist of a single contract or a group of contracts, with segments that have different rates of profitability may be segmented if it meets the criteria in paragraph .40, paragraph .41, or paragraph .42. The criteria for segmenting should be applied consistently to contracts with similar characteristics and in similar circumstances.

.40 A project may be segmented if all the following steps were taken and are documented and verifiable:

- a. The contractor submitted bona fide proposals on the separate components of the project and on the entire project.
- b. The customer had the right to accept the proposals on either basis.
- c. The aggregate amount of the proposals on the separate components approximated the amount of the proposal on the entire project.

.41 A project that does not meet the criteria in paragraph .40 may be segmented only if it meets all the following criteria:

- a. The terms and scope of the contract or project clearly call for separable phases or elements.
- b. The separable phases or elements of the project are often bid or negotiated separately.
- c. The market assigns different gross profit rates to the segments because of factors such as different levels of risk or differences in the relationship of the supply and demand for the services provided in different segments.
- d. The contractor has a significant history of providing similar services to other customers under separate contracts for each significant segment to which a profit margin higher than the overall profit margin on the profit is ascribed.⁷
- e. The significant history with customers who have contracted for services separately is one that is relatively stable in terms of pricing policy rather than one unduly weighted by erratic pricing decisions (responding, for example, to extraordinary economic circumstances or to unique customer-contractor relationships).

⁷ In applying the criterion in paragraph .41(d), values assignable to the segments should be on the basis of the contractor's normal historical prices and terms of such services to other customers. The division considered but rejected the concept of allowing a contractor to segment on the basis of prices charged by other contractors, since it does not follow that those prices could have been obtained by a contractor who has no history in the market.

- f. The excess of the sum of the prices of the separate elements over the price of the total project is clearly attributable to cost savings incident to combined performance of the contract obligations (for example, cost savings in supervision, overhead, or equipment mobilization). Unless this condition is met, segmenting a contract with a price substantially less than the sum of the prices of the separate phases or elements would be inappropriate even if the other conditions are met. Acceptable price variations should be allocated to the separate phases or elements in proportion to the prices ascribed to each. In all other situations a substantial difference in price (whether more or less) between the separate elements and the price of the total project is evidence that the contractor has accepted different profit margins. Accordingly, segmenting is not appropriate, and the contracts should be the profit centers.
- g. The similarity of services and prices in the contract segments and services and the prices of such services to other customers contracted separately should be documented and verifiable.

.42 A production-type contract that does not meet the criteria in paragraphs .40 or .41 may also be segmented and included in groupings such as production lots or releases for the purpose of accumulating and allocating production costs to units produced or delivered on the basis of average unit cost under the conditions specified in paragraph .38.

Measuring Progress on Contracts

.43 This section describes methods of measuring the extent of progress toward completion under the percentage-of-completion method and sets forth criteria for selecting those methods and for determining when a contract is substantially completed. Meaningful measurement of the extent of progress toward completion is essential since this factor is used in determining the amounts of estimated contract revenue and estimated gross profit that will be recognized as earned in any given period.

Methods of Measuring Extent of Progress Toward Completion

.44 In practice, a number of methods are used to measure the extent of progress toward completion. They include the cost-to-cost method, variations of the cost-to-cost method, efforts-expended methods, the units-of-delivery method, and the units-of-work-performed method. Those practices are intended to conform to ARB No. 45, paragraph 4.⁸ Some of the measures are sometimes made and certified by engineers or architects, but management should review and understand the procedures used by those professionals.

.45 Some methods used in practice measure progress toward completion in terms of costs, some in terms of units of work, and some in terms of values

⁸ ARB No. 45, paragraph 4, states:

The committee recommends that the recognized income [under the percentage-of-completion method] be that percentage of estimated total income, either:

(a) that incurred costs to date bear to estimated total costs after giving effect to estimates of costs to complete based upon most recent information, or

(b) that may be indicated by such other measure of progress toward completion as may be appropriate having due regard to work performed.

Costs as here used might exclude, especially during the early stages of a contract, all or a portion of the cost of such items as materials and subcontracts if it appears that such an exclusion would result in a more meaningful periodic allocation of income.

added (the contract value of total work performed to date). All three of these measures of progress are acceptable in appropriate circumstances. The division concluded that other methods that achieve the objective of measuring extent of progress toward completion in terms of costs, units, or value added are also acceptable in appropriate circumstances. However, the method or methods selected should be applied consistently to all contracts having similar characteristics. The method or methods of measuring extent of progress toward completion should be disclosed in the notes to the financial statements. Examples of circumstances not appropriate to some methods are given within the discussion of input and output measures.

Input and Output Measures

.46 The several approaches to measuring progress on a contract can be grouped into input and output measures. Input measures are made in terms of efforts devoted to a contract. They include the methods based on costs and on efforts expended. Output measures are made in terms of results achieved. They include methods based on units produced, units delivered, contract milestones, and value added. For contracts under which separate units of output are produced, progress can be measured on the basis of units of work completed. In other circumstances, progress may be measured, for example, on the basis of cubic yards of excavation for foundation contracts or on the basis of cubic yards of pavement laid for highway contracts.

.47 Both input and output measures have drawbacks in some circumstances. Input is used to measure progress toward completion indirectly, based on an established or assumed relationship between a unit of input and productivity. A significant drawback of input measures is that the relationship of the measures to productivity may not hold, because of inefficiencies or other factors. Output is used to measure results directly and is generally the best measure of progress toward completion in circumstances in which a reliable measure of output can be established. However, output measures often cannot be established, and input measures must then be used. The use of either type of measure requires the exercise of judgment and the careful tailoring of the measure to the circumstances.

.48 The efforts-expended method is an input method based on a measure of the work, such as labor hours, labor dollars, machine hours, or material quantities. Under the labor-hours method, for example, extent of progress is measured by the ratio of hours performed to date to estimated total hours at completion. Estimated total labor hours should include (a) the estimated labor hours of the contractor and (b) the estimated labor hours of subcontractors engaged to perform work for the project, if labor hours of subcontractors are a significant element in the performance of the contract. A labor-hours method can measure the extent of progress in terms of efforts expended only if substantial efforts of subcontractors are included in the computation. If the contractor is unable to obtain reasonably dependable estimates of subcontractors' labor hours at the beginning of the project and as work progresses, he should not use the labor-hours method.

.49 The various forms of the efforts-expended method generally are based on the assumption that profits on contracts are derived from the contractor's efforts in all phases of operations, such as designing, procurement, and management. Profit is not assumed to accrue merely as a result of the acquisition of material or other tangible items used in the performance of the contract or the awarding of subcontracts. As previously noted, a significant drawback of

efforts-expended methods is that the efforts included in the measure may not all be productive.

.50 Measuring progress toward completion based on the ratio of costs incurred to total estimated costs is also an input method. Some of the costs incurred, particularly in the early stages of the contract, should be disregarded in applying this method because they do not relate to contract performance. These include the costs of items such as uninstalled materials not specifically produced or fabricated for the project or of subcontracts that have not been performed. For example, for construction projects, the cost of materials not unique to the project that have been purchased or accumulated at job sites but that have not been physically installed do not relate to performance.⁹ The costs of such materials should be excluded from costs incurred for the purpose of measuring the extent of progress toward completion. Also, the cost of equipment purchased for use on a contract should be allocated over the period of its expected use unless title to the equipment is transferred to the customer by terms of the contract. For production-type contracts, the complement of expensive components (for example, computers, engines, radars, and complex “black boxes”) to be installed into the deliverable items may aggregate a significant portion of the total cost of the contract. In some circumstances, the costs incurred for such components, even though the components were specifically purchased for the project, should not be included in the measurement before the components are installed if inclusion would tend to overstate the percentage of completion otherwise determinable.

.51 The acceptability of the results of input or output measures deemed to be appropriate to the circumstances should be periodically reviewed and confirmed by alternative measures that involve observation and inspection. For example, the results provided by the measure used to determine the extent of progress may be compared to the results of calculations based on physical observations by engineers, architects, or similarly qualified personnel. That type of review provides assurance somewhat similar to that provided for perpetual inventory records by periodic physical inventory counts.

Completion Criteria Under the Completed-Contract Method

.52 As a general rule, a contract may be regarded as substantially completed if remaining costs and potential risks are insignificant in amount. The overriding objectives are to maintain consistency in determining when contracts are substantially completed and to avoid arbitrary acceleration or deferral of income. The specific criteria used to determine when a contract is substantially completed should be followed consistently and should be disclosed in the note to the financial statements on accounting policies. Circumstances to be considered in determining when a project is substantially completed include, for example, delivery of the product, acceptance by the customer, departure from the site, and compliance with performance specifications.

Income Determination—Revenue Elements

.53 Estimating the revenue on a contract is an involved process, which is affected by a variety of uncertainties that depend on the outcome of a series of

⁹ The cost of uninstalled materials specifically produced, fabricated, or constructed for a project should be included in the costs used to measure extent of progress. Such materials consist of items unique to a project that a manufacturer or supplier does not carry in inventory and that must be produced or altered to meet the specifications of the project.

future events. The estimates must be periodically revised throughout the life of the contract as events occur and as uncertainties are resolved.

.54 The major factors that must be considered in determining total estimated revenue include the basic contract price, contract options, change orders, claims, and contract provisions for penalties and incentive payments, including award fees and performance incentives. All those factors and other special contract provisions must be evaluated throughout the life of a contract in estimating total contract revenue to recognize revenues in the periods in which they are earned under the percentage-of-completion method of accounting.

Basic Contract Price—General

.55 The estimated revenue from a contract is the total amount that a contractor expects to realize from the contract. It is determined primarily by the terms of the contract and the basic contract price. Contract price may be relatively fixed or highly variable and subject to a great deal of uncertainty, depending on the type of contract involved. Appendix B describes basic contract types and major variations in the basic types. The total amount of revenue that ultimately will be realized on a contract is often subject to a variety of changing circumstances and accordingly may not be known with certainty until the parties to the contract have fully performed their obligations. Thus, the determination of total estimated revenue requires careful consideration and the exercise of judgment in assessing the probabilities of future outcomes.

.56 Although fixed-price contracts usually provide for a stated contract price, a specified scope of the work to be performed, and a specified performance schedule, they sometimes have adjustment schedules based on application of economic price adjustment (escalation), price redetermination, incentive, penalty, and other pricing provisions. Determining contract revenue under unit-price contracts generally involves the same factors as under fixed-price contracts. Determining contract revenue from a time-and-material contract requires a careful analysis of the contract, particularly if the contract includes guaranteed maximums or assigns markups to both labor and materials; and the determination involves consideration of some of the factors discussed below in regard to cost-type contracts.

Basic Contract Price—Cost-Type Contracts

.57 Cost-type contracts have a variety of forms (see Appendix B). The various forms have differing contract terms that affect accounting, such as provisions for reimbursable costs (which are generally spelled out in the contract), overhead recovery percentages, and fees. A fee may be a fixed amount or a percentage of reimbursable costs or an amount based on performance criteria.¹⁰ Generally, percentage fees may be accrued as the related costs are incurred, since they are a percentage of costs incurred, and profits should therefore be recognized as costs are incurred. Cost-type contracts often include provisions for guaranteed maximum total reimbursable costs or target penalties and rewards relating to underruns and overruns of predetermined target prices, completion dates, plant capacity on completion of the project, or other criteria.

.58 One problem peculiar to cost-type contracts involves the determination of the amounts of reimbursable costs that should be reflected as revenue. Under some contracts, particularly service-type contracts, a contractor acts sol-

¹⁰ Cost-type government contracts with fees based on a percentage of cost are no longer granted under government regulations.

ely in the capacity of an agent (construction manager) and has no risks associated with costs managed. This relationship may arise, for example, if an owner awards a construction management contract to one entity and a construction contract to another. If the contractor, serving as the construction manager, acts solely as an agent, his revenue should include only the fee and should exclude subcontracts negotiated or managed on behalf of the owner and materials purchased on behalf of the owner.

.59 In other circumstances, a contractor acts as an ordinary principal under a cost-type contract. For example, the contractor may be responsible to employees for salaries and wages and to subcontractors and other creditors for materials and services, and he may have the discretionary responsibility to procure and manage the resources in performing the contract. The contractor should include in revenue all reimbursable costs for which he has risk or on which his fee was based at the time of bid or negotiation. In addition, revenue from overhead percentage recoveries and the earned fee should be included in revenue.

Customer-Furnished Materials

.60 Another concern associated with measuring revenue relates to materials furnished by a customer or purchased by the contractor as an agent for the customer. Often, particularly for large, complex projects, customers may be more capable of carrying out the procurement function or may have more leverage with suppliers than the contractor. In those circumstances, the contractor generally informs the customer of the nature, type, and characteristics or specifications of the materials required and may even purchase the required materials and pay for them, using customer purchase orders and checks drawn against the customer's bank account. If the contractor is responsible for the nature, type, characteristics, or specifications of material that the customer furnishes or that the contractor purchases as an agent of the customer, or if the contractor is responsible for the ultimate acceptability of performance of the project based on such material, the value of those items should be included as contract price and reflected as revenue and costs in periodic reporting of operations. As a general rule, revenues and costs should include all items for which the contractor has an associated risk, including items on which his contractual fee was based.

Change Orders

.61 Change orders are modifications of an original contract that effectively change the provisions of the contract without adding new provisions. They may be initiated by either the contractor or the customer, and they include changes in specifications or design, method or manner of performance, facilities, equipment, materials, sites, and period for completion of the work. Many change orders are unpriced; that is, the work to be performed is defined, but the adjustment to the contract price is to be negotiated later. For some change orders, both scope and price may be unapproved or in dispute. Accounting for change orders depends on the underlying circumstances, which may differ for each change order depending on the customer, the contract, and the nature of the change. Change orders should therefore be evaluated according to their characteristics and the circumstances in which they occur. In some circumstances, change orders as a normal element of a contract may be numerous, and separate identification may be impractical. Such change orders may be evaluated statistically on a composite basis using historical results as modified by current conditions. If such change orders are considered by the parties to be a normal element within the original scope of the contract, no

change in the contract price is required. Otherwise, the adjustment to the contract price may be routinely negotiated. Contract revenue and costs should be adjusted to reflect change orders approved by the customer and the contractor regarding both scope and price.

.62 Accounting for unpriced change orders depends on their characteristics and the circumstances in which they occur. Under the completed-contract method, costs attributable to unpriced change orders should be deferred as contract costs if it is probable that aggregate contract costs, including costs attributable to change orders, will be recovered from contract revenues. For all unpriced change orders, recovery should be deemed probable if the future event or events necessary for recovery are likely to occur. Some of the factors to consider in evaluating whether recovery is probable are the customer's written approval of the scope of the change order, separate documentation for change order costs that are identifiable and reasonable, and the entity's favorable experience in negotiating change orders, especially as it relates to the specific type of contract and change order being evaluated. The following guidelines should be followed in accounting for unpriced change orders under the percentage-of-completion method.

- a. Costs attributable to unpriced change orders should be treated as costs of contract performance in the period in which the costs are incurred if it is *not* probable that the costs will be recovered through a change in the contract price.
- b. If it is probable that the costs will be recovered through a change in the contract price, the costs should be deferred (excluded from the cost of contract performance) until the parties have agreed on the change in contract price, or, alternatively, they should be treated as costs of contract performance in the period in which they are incurred, and contract revenue should be recognized to the extent of the costs incurred.
- c. If it is probable that the contract price will be adjusted by an amount that exceeds the costs attributable to the change order and the amount of the excess can be reliably estimated, the original contract price should also be adjusted for that amount when the costs are recognized as costs of contract performance if its realization is probable. However, since the substantiation of the amount of future revenue is difficult, revenue in excess of the costs attributable to unpriced change orders should only be recorded in circumstances in which realization is assured beyond a reasonable doubt, such as circumstances in which an entity's historical experience provides such assurance or in which an entity has received a bona fide pricing offer from a customer and records only the amount of the offer as revenue.

.63 If change orders are in dispute or are unapproved in regard to both scope and price, they should be evaluated as claims (see paragraphs .65–.67).

Contract Options and Additions

.64 An option or an addition to an existing contract should be treated as a separate contract in any of the following circumstances:

- a. The product or service to be provided differs significantly from the product or service provided under the original contract.
- b. The price of the new product or service is negotiated without regard to the original contract and involves different economic judgments.

- c. The products or services to be provided under the exercised option or amendment are similar to those under the original contract, but the contract price and anticipated contract cost relationship are significantly different.

If an option or addition to an existing contract does not meet any of the above conditions, it may be combined with the original contract if it meets the criteria in paragraph .37 or .38. Exercised options or additions that do not meet the criteria for treatment as separate contracts or for combining with the original contracts should be treated as change orders on the original contracts.

Claims

.65 Claims are amounts in excess of the agreed contract price (or amounts not included in the original contract price) that a contractor seeks to collect from customers or others for customer-caused delays, errors in specifications and designs, contract terminations, change orders in dispute or unapproved as to both scope and price, or other causes of unanticipated additional costs. Recognition of amounts of additional contract revenue relating to claims is appropriate only if it is probable that the claim will result in additional contract revenue and if the amount can be reliably estimated. Those two requirements are satisfied by the existence of all the following conditions:

- a. The contract or other evidence provides a legal basis for the claim; or a legal opinion has been obtained, stating that under the circumstances there is a reasonable basis to support the claim.
- b. Additional costs are caused by circumstances that were unforeseen at the contract date and are not the result of deficiencies in the contractor's performance.
- c. Costs associated with the claim are identifiable or otherwise determinable and are reasonable in view of the work performed.
- d. The evidence supporting the claim is objective and verifiable, not based on management's "feel" for the situation or on unsupported representations.

If the foregoing requirements are met, revenue from a claim should be recorded only to the extent that contract costs relating to the claim have been incurred. The amounts recorded, if material, should be disclosed in the notes to the financial statements. Costs attributable to claims should be treated as costs of contract performance as incurred.

.66 However, a practice such as recording revenues from claims only when the amounts have been received or awarded may be used. If that practice is followed, the amounts should be disclosed in the notes to the financial statements.

.67 If the requirements in paragraph .65 are not met or if those requirements are met but the claim exceeds the recorded contract costs, a contingent asset should be disclosed in accordance with FASB Statement No. 5, paragraph 17.

Income Determination—Cost Elements

.68 Contract costs must be identified, estimated, and accumulated with a reasonable degree of accuracy in determining income earned. At any time during the life of a contract, total estimated contract cost consists of two components: costs incurred to date and estimated cost to complete the contract. A company should be able to determine costs incurred on a contract with a relatively high degree of precision, depending on the adequacy and effectiveness of its cost accounting system. The procedures or systems used in accounting for

costs vary from relatively simple, manual procedures that produce relatively modest amounts of detailed analysis to sophisticated, computer-based systems that produce a great deal of detailed analysis. Despite the diversity of systems and procedures, however, an objective of each system or of each set of procedures should be to accumulate costs properly and consistently by contract with a sufficient degree of accuracy to assure a basis for the satisfactory measurement of earnings.

Contract Costs

.69 Contract costs are accumulated in the same manner as inventory costs and are charged to operations as the related revenue from contracts is recognized. Contract costs generally include all direct costs, such as materials, direct labor, and subcontracts, and indirect costs identifiable with or allocable to the contracts. However, practice varies for certain types of indirect costs considered allocable to contracts, for example, support costs (such as central preparation and processing of job payrolls, billing and collection costs, and bidding and estimating costs).

.70 Authoritative accounting pronouncements require costs to be considered period costs if they cannot be clearly related to production, either directly or by an allocation based on their discernible future benefits.

.71 Income is recognized over the term of the contract under the percentage-of-completion method or is recognized as units are delivered under the units-of-delivery modification and is deferred until performance is substantially complete under the completed-contract method. None of the characteristics peculiar to those methods, however, require accounting for contract costs to deviate in principle from the basic framework established in existing authoritative literature applicable to inventories or business enterprises in general.

.72 A contracting entity should apply the following general principles in accounting for costs of construction-type and those production-type contracts covered by this statement. The principles are consistent with generally accepted accounting principles for inventory and production costs in other areas, and their application requires the exercise of judgment.

- a. All direct costs, such as material, labor, and subcontracting costs, should be included in contract costs.
- b. Indirect costs allocable to contracts include the costs of indirect labor, contract supervision, tools and equipment, supplies, quality control and inspection, insurance, repairs and maintenance, depreciation and amortization, and, in some circumstances, support costs, such as central preparation and processing of payrolls. For government contractors, other types of costs that are allowable or allocable under pertinent government contract regulations may be allocated to contracts as indirect costs if otherwise allowable under GAAP.¹¹ Methods of allocating indirect costs should be systematic and rational. They include, for example, allocations based on direct labor costs, direct

¹¹ The AICPA Audit and Accounting Guide *Federal Government Contractors* states, "Practice varies among government contractors concerning the extent to which costs are included in inventory. Some contractors include in inventory all direct costs and only certain indirect costs. . . . Other contractors record as inventory all costs identified with the contract, including an allocation of general and administrative . . . expenses." The guide points out that many accountants believe that the practice of allocating general and administrative expenses to contract costs, which is permitted under the completed-contract method by ARB No. 45, paragraph 10, may appropriately be extended to government contracts because they believe that "costs incurred pursuant to a government contract are associated directly with the contract's revenue, and both should be recognized in the same period." [Footnote revised, April 1996, to reflect conforming changes necessary due to the issuance of recent authoritative literature.]

- labor hours, or a combination of direct labor and material costs. The appropriateness of allocations of indirect costs and of the methods of allocation depend on the circumstances and involve judgment.
- c. General and administrative costs ordinarily should be charged to expense as incurred but may be accounted for as contract costs under the completed-contract method of accounting¹² or, in some circumstances, as indirect contract costs by government contractors.¹³
 - d. Selling costs should be excluded from contract costs and charged to expense as incurred unless they meet the criteria for precontract costs in paragraph .75.
 - e. Costs under cost-type contracts should be charged to contract costs in conformity with generally accepted accounting principles in the same manner as costs under other types of contracts because unrealistic profit margins may result in circumstances in which reimbursable cost accumulations omit substantial contract costs (with a resulting larger fee) or include substantial unallocable general and administrative costs (with a resulting smaller fee).
 - f. In computing estimated gross profit or providing for losses on contracts, estimates of cost to complete should reflect all of the types of costs included in contract costs.
 - g. Inventoriable costs should not be carried at amounts that when added to the estimated cost to complete are greater than the estimated realizable value of the related contracts.

Interest costs should be accounted for in accordance with FASB Statement No. 34, *Capitalization of Interest Cost*.

Precontract Costs

.73 In practice, costs are deferred in anticipation of future contract sales in a variety of circumstances. The costs may consist of (a) costs incurred in anticipation of a specific contract that will result in no future benefit unless the contract is obtained (such as the costs of mobilization, engineering, architectural, or other services incurred on the basis of commitments or other indications of interest in negotiating a contract), (b) costs incurred for assets to be used in connection with specific anticipated contracts (for example, costs for the purchase of production equipment, materials, or supplies), (c) costs incurred to acquire or produce goods in excess of the amounts required under a contract in anticipation of future orders for the same item, and (d) learning, start-up, or mobilization costs incurred for anticipated but unidentified contracts.

.74 Learning or start-up costs are sometimes incurred in connection with the performance of a contract or a group of contracts. In some circumstances, follow-on or future contracts for the same goods or services are anticipated. Such costs usually consist of labor, overhead, rework, or other special costs that must be incurred to complete the existing contract or contracts in progress and

¹² Paragraph 10 of ARB No. 45, *Long-Term Construction-Type Contracts*, states:

When the completed-contract method is used, it may be appropriate to allocate general and administrative expenses to contract costs rather than to periodic income. This may result in a better matching of costs and revenues than would result from treating such expenses as period cost, particularly in years when no contracts were completed.

¹³ See the discussion of the AICPA Audit and Accounting Guide *Federal Government Contractors* in footnote 11. [Footnote revised, April 1996, to reflect conforming changes necessary due to the issuance of recent authoritative literature.]

are distinguished from research and development costs.¹⁴ A direct relationship between such costs and the anticipated future contracts is often difficult to establish, and the receipt of future contracts often cannot reasonably be anticipated.

.75 The division recommends the following accounting for precontract costs:

- a. Costs that are incurred for a specific anticipated contract and that will result in no future benefits unless the contract is obtained should not be included in contract costs or inventory before the receipt of the contract. However, such costs may be otherwise deferred, subject to evaluation of their probable recoverability, but only if the costs can be directly associated with a specific anticipated contract and if their recoverability from that contract is probable.[‡]
- b. Costs incurred for assets, such as costs for the purchase of materials, production equipment, or supplies, that are expected to be used in connection with anticipated contracts may be deferred outside the contract cost or inventory classification if their recovery from future contract revenue or from other dispositions of the assets is probable.
- c. Costs incurred to acquire or produce goods in excess of the amounts required for an existing contract in anticipation of future orders for the same items may be treated as inventory if their recovery is probable.
- d. Learning or start-up costs incurred in connection with existing contracts and in anticipation of follow-on or future contracts for the same goods or services should be charged to existing contracts.^[15]
- e. Costs appropriately deferred in anticipation of a contract should be included in contract costs on the receipt of the anticipated contract.
- f. Costs related to anticipated contracts that are charged to expenses as incurred because their recovery is not considered probable should not be reinstated by a credit to income on the subsequent receipt of the contract.

Cost Adjustments Arising From Back Charges

.76 Back charges are billings for work performed or costs incurred by one party that, in accordance with the agreement, should have been performed or incurred by the party to whom billed. These frequently are disputed items. For example, owners bill back charges to general contractors, and general contractors bill back charges to subcontractors. Examples of back charges include charges for cleanup work and charges for a subcontractor's use of a general contractor's equipment.

.77 A common practice is to net back charges in the estimating process. The division recommends the following procedures in accounting for back charges:

- Back charges to others should be recorded as receivables and, to the extent considered collectible, should be applied to reduce contract costs.

¹⁴ FASB Statement No. 2, *Accounting for Research and Development Costs*, requires that research and development costs be charged to expense when incurred.

[‡] SOP 98-5, *Reporting on the Costs of Start-Up Activities*, amends this SOP by requiring precontract costs that are start-up activities to be expensed as incurred if they are determined to be within the scope of SOP 98-5. [Footnote revised, July 2002, to reflect conforming changes necessary due to the issuance of Statement of Position 98-5.]

^[15] [Footnote deleted, April 1996, to reflect conforming changes necessary due to the issuance of recent authoritative literature.]

However, if the billed party disputes the propriety or amount of the charge, the back charge is in effect a claim, and the criteria for recording claims apply.

- Back charges from others should be recorded as payables and as additional contract costs to the extent that it is probable that the amounts will be paid.

Estimated Cost to Complete

.78 The estimated cost to complete, the other component of total estimated contract cost, is a significant variable in the process of determining income earned and is thus a significant factor in accounting for contracts. The latest estimate may be determined in a variety of ways and may be the same as the original estimate. Practices in estimating total contract costs vary, and guidance is needed in this area because of the impact of those practices on accounting. The following practices should be followed:

- a. Systematic and consistent procedures that are correlated with the cost accounting system should be used to provide a basis for periodically comparing actual and estimated costs.
- b. In estimating total contract costs, the quantities and prices of all significant elements of cost should be identified.
- c. The estimating procedures should provide that estimated cost to complete includes the same elements of cost that are included in actual accumulated costs; also, those elements should reflect expected price increases.
- d. The effects of future wage and price escalations should be taken into account in cost estimates, especially when the contract performance will be carried out over a significant period of time. Escalation provisions should not be blanket overall provisions but should cover labor, materials, and indirect costs based on percentages or amounts that take into consideration experience and other pertinent data.
- e. Estimates of cost to complete should be reviewed periodically and revised as appropriate to reflect new information.

Computation of Income Earned for a Period Under the Percentage-of-Completion Method

.79 Total estimated gross profit on a contract, the difference between total estimated contract revenue and total estimated contract cost, must be determined before the amount earned on the contract for a period can be determined. The portion of total revenue earned or the total amount of gross profit earned to date is determined by the measurement of the extent of progress toward completion using one of the methods discussed in paragraphs .44 to .51 of this statement. The computation of income earned for a period involves a determination of the portion of total estimated contract revenue that has been earned to date (earned revenue) and the portion of total estimated contract cost related to that revenue (cost of earned revenue). Two different approaches to determining earned revenue and cost of earned revenue are widely used in practice. Either of the alternative approaches may be used on a consistent basis.¹⁶

¹⁶ The use of Alternative A in the discussion and in the presentation of some of the provisions of this statement is for convenience and consistency and is not intended to imply that Alternative A is the preferred approach.

Alternative A

.80 The advocates of this method believe that the portion of total estimated contract revenue earned to date should be determined by the measurement of the extent of progress toward completion and that, in accordance with the matching concept, the measurement of extent of progress toward completion should also be used to allocate a portion of total estimated contract cost to the revenue recognized for the period. They believe that this procedure results in reporting earned revenue, cost of earned revenue, and gross profit consistent with the measurement of contract performance. Moreover, they believe that, if there are no changes in estimates during the performance of a contract, the procedure also results in a consistent gross profit percentage from period to period. However, they recognize that a consistent gross profit percentage is rarely obtained in practice because of the need to be responsive in the accounting process to changes in estimates of contract revenues, costs, earned revenue, and gross profits. In accordance with this procedure, earned revenue, cost of earned revenue, and gross profit should be determined as follows:

- a. *Earned Revenue* to date should be computed by multiplying total estimated contract revenue by the percentage of completion (as determined by one of the acceptable methods of measuring the extent of progress toward completion). The excess of the amount over the earned revenue reported in prior periods is the earned revenue that should be recognized in the income statement for the current period.
- b. *Cost of Earned Revenue* for the period should be computed in a similar manner. Cost of earned revenue to date should be computed by multiplying total estimated contract cost by the percentage of completion on the contract. The excess of that amount over the cost of earned revenue reported in prior periods is the cost of earned revenue that should be recognized in the income statement for the current period. The difference between total cost incurred to date and cost of earned revenue to date should be reported on the balance sheet.
- c. *Gross Profit* on a contract for a period is the excess of earned revenue over the cost of earned revenue.

Alternative B

.81 The advocates of this method believe that the measurement of the extent of progress toward completion should be used to determine the amount of gross profit earned to date and that the earned revenue to date is the sum of the total cost incurred on the contract and the amount of gross profit earned. They believe that the cost of work performed on a contract for a period, including materials, labor, subcontractors, and other costs, should be the cost of earned revenue for the period. They believe that the amount of costs incurred can be objectively determined, does not depend on estimates, and should be the amount that enters into the accounting determination of income earned. They recognize that, under the procedure that they advocate, gross profit percentages will vary from period to period unless the cost-to-cost method is used to measure the extent of progress toward completion. However, they believe that varying profit percentages are consistent with the existing authoritative literature when costs incurred do not provide an appropriate measure of the extent of progress toward completion. In accordance with Alternative B, earned revenue, cost of earned revenue, and gross profit are determined as follows:

- a. *Earned Revenue* is the amount of gross profit earned on a contract for a period plus the costs incurred on the contract during the period.
- b. *Cost of Earned Revenue* is the cost incurred during the period, excluding the cost of materials not unique to a contract that have not been used for the contract and costs incurred for subcontracted work that is still to be performed.
- c. *Gross Profit* earned on a contract should be computed by multiplying the total estimated gross profit on the contract by the percentage of completion (as determined by one of the acceptable methods of measuring extent of progress toward completion). The excess of that amount over the amount of gross profit reported in prior periods is the earned gross profit that should be recognized in the income statement for the current period.

Revised Estimates

.82 Adjustments to the original estimates of the total contract revenue, total contract cost, or extent of progress toward completion are often required as work progresses under the contract and as experience is gained, even though the scope of the work required under the contract may not change. The nature of accounting for contracts is such that refinements of the estimating process for changing conditions and new developments are continuous and characteristic of the process. Additional information that enhances and refines the estimating process is often obtained after the balance sheet date but before the issuance of the financial statements; such information should result in an adjustment of the unissued financial statements. Events occurring after the date of the financial statements that are outside the normal exposure and risk aspects of the contract should not be considered refinements of the estimating process of the prior year but should be disclosed as subsequent events.

.83 Revisions in revenue, cost, and profit estimates or in measurements of the extent of progress toward completion are changes in accounting estimates and, as such, should be accounted for in accordance with FASB Statement No. 154, *Accounting Changes and Error Corrections—a replacement of APB Opinion No. 20 and FASB Statement No. 3*.^[17] A change in accounting estimate shall be accounted for in (a) the period of change if the change affects that period only or (b) the period of change and future periods if the change affects both. A change in accounting estimate shall not be accounted for by restating or retrospectively adjusting amounts reported in financial statements of prior periods or by reporting pro forma amounts for prior periods. FASB Statement No. 154 carries forward the following two alternative methods of accounting for changes in accounting estimates identified in APB Opinion No. 20, *Accounting Changes*:

- *Cumulative Catch-up*. Account for the change in estimate in the period of change so that the balance sheet at the end of the period of change and the accounting in subsequent periods are as they would have been if the revised estimate had been the original estimate.
- *Reallocation*. Account for the effect of the change ratably over the period of change in estimate and subsequent periods.

^[17] [Footnote deleted, June 2007, to reflect conforming changes necessary due to the issuance of recent authoritative literature.]

Although both methods are used in practice to account for changes in estimates of total revenue, total costs, or extent of progress under the percentage-of-completion method, the cumulative catch-up method is more widely used. Accordingly, to narrow the areas of differences in practice, such changes should be accounted for by the cumulative catch-up method. [Paragraph revised, June 2007, to reflect conforming changes necessary due to the issuance of FASB Statement No. 154.]

.84 Although estimating is a continuous and normal process for contractors, FASB Statement No. 154, paragraph 22 requires disclosure of the effect of significant revisions if the effect is material.^[18] The effect on income from continuing operations, net income (or other appropriate captions of changes in the applicable net assets or performance indicator), and any related per-share amounts of the current period shall be disclosed for a change in estimate that affects several future periods. If a change in estimate does not have a material effect in the period of change but is reasonably certain to have a material effect in later periods, a description of that change in estimate shall be disclosed whenever the financial statements of the period of change are presented. [Paragraph revised, June 2007, to reflect conforming changes necessary due to the issuance of FASB Statement No. 154.]

Provisions for Anticipated Losses on Contracts

.85 When the current estimates of total contract revenue and contract cost indicate a loss, a provision for the entire loss on the contract should be made. Provisions for losses should be made in the period in which they become evident under either the percentage-of-completion method or the completed-contract method. If a group of contracts are combined based on the criteria in paragraph .37 or .38, they should be treated as a unit in determining the necessity for a provision for a loss. If contracts are segmented based on the criteria in paragraph .40, .41, or .42 of this statement, the individual segments should be considered separately in determining the need for a provision for a loss.

.86 Losses on cost-type contracts, although less frequent, may arise if, for example, a contract provides for guaranteed maximum reimbursable costs or target penalties. In recognizing losses for accounting purposes, the contractor's normal cost accounting methods should be used in determining the total cost overrun on the contract, and losses should include provisions for performance penalties.

.87 The costs used in arriving at the estimated loss on a contract should include all costs of the type allocable to contracts under paragraph .72 of this statement. Other factors that should be considered in arriving at the projected loss on a contract include target penalties and rewards, nonreimbursable costs on cost-plus contracts, change orders, and potential price redeterminations. In circumstances in which general and administrative expenses are treated as contract costs under the completed-contract method of accounting, the estimated loss should include the same types of general and administrative expenses.

.88 The provision for loss arises because estimated cost for the contract exceeds estimated revenue. Consequently, the provision for loss should be accounted for in the income statement as an additional contract cost rather

^[18] [Footnote deleted, June 2007, to reflect conforming changes necessary due to the issuance of recent authoritative literature.]

than as a reduction of contract revenue, which is a function of contract price, not cost. Unless the provision is material in amount or unusual or infrequent in nature, the provision should be included in contract cost and need not be shown separately in the income statement. If it is shown separately, it should be shown as a component of the cost included in the computation of gross profit.

.89 Provisions for losses on contracts should be shown separately as liabilities on the balance sheet, if significant, except in circumstances in which related costs are accumulated on the balance sheet, in which case the provisions may be deducted from the related accumulated costs. In a classified balance sheet, a provision shown as a liability should be shown as a current liability.


Transition

.90 An accounting change from the completed-contract method or from the percentage-of-completion method to conform to the recommendations of this statement of position should be made retrospectively by restating the financial statements of prior periods. The restatement should be made on the basis of current information if historical information is not available. If the information for restatement of prior periods is not available on either a historical or current basis, financial statements and summaries should be restated for as many consecutive prior periods preceding the transition date of this statement as is practicable, and the cumulative effect on the retained earnings at the beginning of the earliest period restated (or at the beginning of the period in which the statement is first applied if it is not practicable to restate any prior periods) should be included in determining net income for that period (see paragraphs 8 and 9 of FASB Statement No. 154). [Paragraph revised, June 2007, to reflect conforming changes necessary due to the issuance of FASB Statement No. 154.]

.91 Accounting changes to conform to the recommendations of this statement of position, other than those stated in paragraph .90, should be made prospectively for contracting transactions, new contracts, and contract revisions entered into on or after the effective date of this statement. The division recommends the application of the provisions of this statement for fiscal years, and interim periods in such fiscal years, beginning after June 30, 1981. The division encourages earlier application of this statement, including retroactive application to all contracts regardless of when they were entered into. Disclosures should be made in the financial statements in the period of change in accordance with paragraph 17 of FASB Statement No. 154. [Paragraph revised, June 2007, to reflect conforming changes necessary due to the issuance of FASB Statement No. 154.]


Appendix A

Schematic Chart of SOP Organization

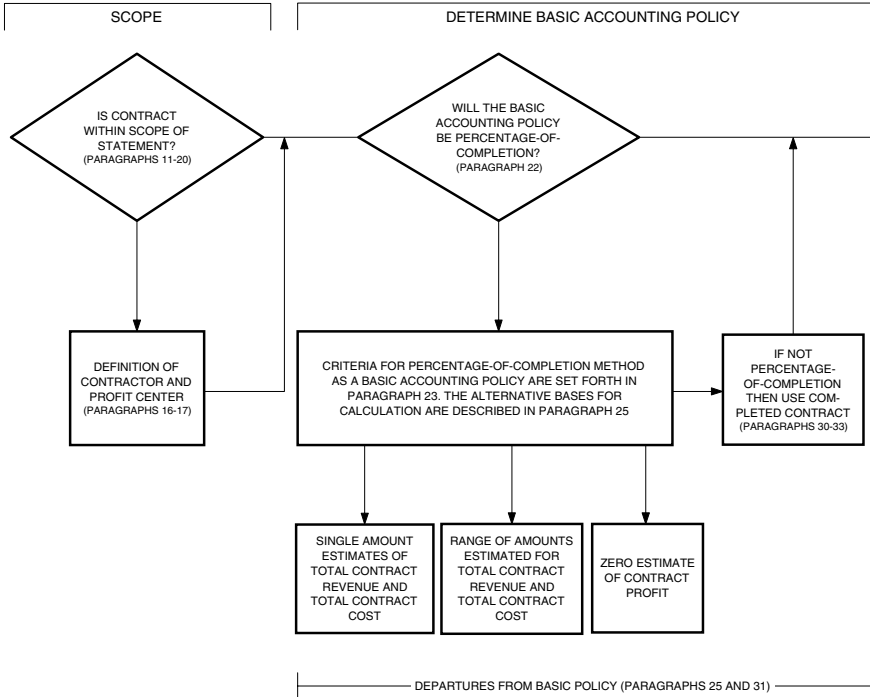

NOTE: ALL PARAGRAPH NUMBERS ABOVE REFER TO TEXT OF SOP.

* If computation results in a loss, see paragraphs 85-89

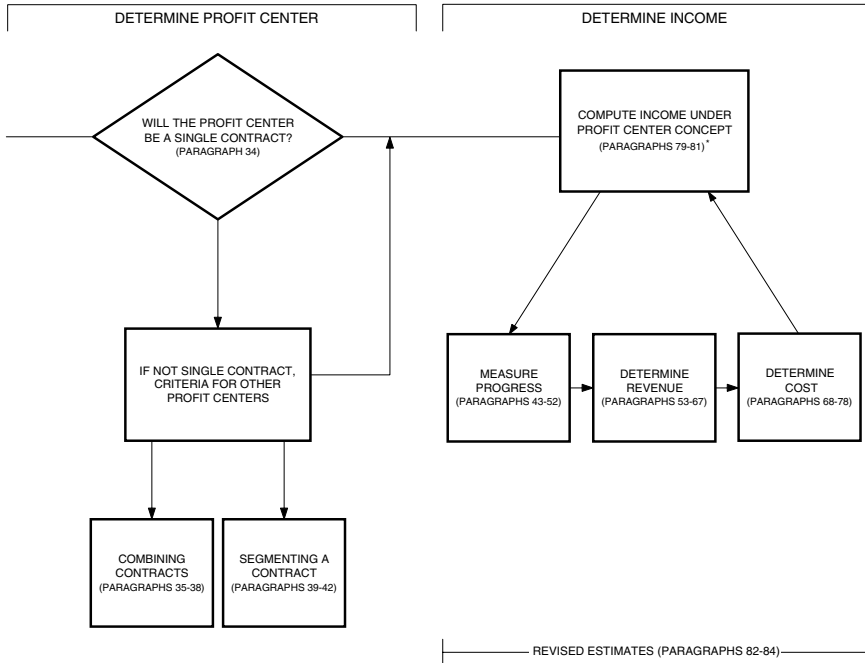

Appendix B

Types of Contracts

Four basic types of contracts are distinguished on the basis of their pricing arrangements in paragraph .15 of this statement: (a) fixed-price or lump-sum contracts, (b) time-and-material contracts, (c) cost-type (including cost-plus) contracts, and (d) unit-price contracts. This appendix describes the basic types of contracts in greater detail and briefly describes common variations of each basic type.

Fixed-Price or Lump-Sum Contracts

A fixed-price or lump-sum contract is a contract in which the price is not usually subject to adjustment because of costs incurred by the contractor. Common variations of fixed-price contracts are:

1. *Firm fixed-price contract*—A contract in which the price is not subject to any adjustment by reason of the cost experience of the contractor or his performance under the contract.
2. *Fixed-price contract with economic price adjustment*—A contract which provides for upward or downward revision of contract price upon the occurrence of specifically defined contingencies, such as increases or decreases in material prices or labor wage rates.
3. *Fixed-price contract providing for prospective periodic redetermination of price*—A contract which provides a firm fixed-price for an initial number of unit deliveries or for an initial period of performance and for prospective price redeterminations either upward or downward at stated intervals during the remaining period of performance under the contract.
4. *Fixed-price contract providing for retroactive redetermination of price*—A contract which provides for a ceiling price and retroactive price redetermination (within the ceiling price) after the completion of the contract, based on costs incurred, with consideration being given to management ingenuity and effectiveness during performance.
5. *Fixed-price contract providing for firm target cost incentives*—A contract which provides at the outset for a firm target cost, a firm target profit, a price ceiling (but not a profit ceiling or floor), and a formula (based on the relationship which final negotiated total cost bears to total target cost) for establishing final profit and price.
6. *Fixed-price contract providing for successive target cost incentives*—A contract which provides at the outset for an initial target cost, an initial target profit, a price ceiling, a formula for subsequently fixing the firm target profit (within a ceiling and a floor established along with the formula, at the outset), and a production point at which the formula will be applied.
7. *Fixed-price contract providing for performance incentives*—A contract which incorporates an incentive to the contractor to surpass stated performance targets by providing for increases in the profit to the extent that such targets are surpassed and for decreases to the extent that such targets are not met.

8. *Fixed-price level-of-effort term contract*—A contract which usually calls for investigation or study in a specific research and development area. It obligates the contractor to devote a specified level of effort over a stated period of time for a fixed dollar amount.¹

Time-and-Material Contracts

Time-and-material contracts are contracts that generally provide for payments to the contractor on the basis of direct labor hours at fixed hourly rates (that cover the cost of direct labor and indirect expenses and profit) and cost of materials or other specified costs. Common variations of time and material contracts are:

1. Time at marked-up rate.
2. Time at marked-up rate, material at cost.
3. Time and material at marked-up rates.
4. Guaranteed maximum cost—labor only or labor and material.

Cost-Type Contracts

Cost-type contracts provide for reimbursement of allowable or otherwise defined costs incurred plus a fee that represents profit. Cost-type contracts usually only require that the contractor use his best efforts to accomplish the scope of the work within some specified time and some stated dollar limitation. Common variations of cost-plus contracts are

1. *Cost-sharing contract*—A contract under which the contractor is reimbursed only for an agreed portion of costs and under which no provision is made for a fee.
2. *Cost-without-fee contract*—A contract under which the contractor is reimbursed for costs with no provision for a fee.
3. *Cost-plus-fixed-fee contract*—A contract under which the contractor is reimbursed for costs plus the provision for a fixed fee.
4. *Cost-plus-award-fee contract*—A contract under which the contractor is reimbursed for costs plus a fee consisting of two parts: (a) a fixed amount which does not vary with performance and (b) an award amount based on performance in areas such as quality, timeliness, ingenuity, and cost-effectiveness. The amount of award fee is based upon a subjective evaluation by the government of the contractor's performance judged in light of criteria set forth in the contract.
5. *Cost-plus-incentive-fee contract (Incentive based on cost)*—A contract under which the contractor is reimbursed for costs plus a fee which is adjusted by formula in accordance with the relationship which total allowable costs bear to target cost. At the outset there is negotiated a target cost, a target fee, a minimum and maximum fee, and the adjustment formula.

¹ AICPA Audit and Accounting Guide *Federal Government Contractors*, chapter 1. [Footnote revised, April 1996, to reflect conforming changes necessary due to the issuance of recent authoritative literature.]

6. *Cost-plus-incentive-fee contract (Incentive based on performance)*—A contract under which a contractor is reimbursed for costs plus an incentive to surpass stated performance targets by providing for increases in the fee to the extent that such targets are surpassed and for decreases to the extent that such targets are not met.²

Unit-Price Contracts

Unit-price contracts are contracts under which the contractor is paid a specified amount for every unit of work performed. A unit-price contract is essentially a fixed-price contract with the only variable being units of work performed. Variations in unit-price contracts include the same type of variations as fixed-price contracts. A unit-price contract is normally awarded on the basis of a total price that is the sum of the product of the specified units and unit prices. The method of determining total contract price may give rise to unbalanced unit prices because units to be delivered early in the contract may be assigned higher unit prices than those to be delivered as the work under the contract progresses.

² AICPA Audit and Accounting Guide *Federal Government Contractors*, chapter 1. [Footnote revised, April 1996, to reflect conforming changes necessary due to the issuance of recent authoritative literature.]

Appendix C

Summary of Disclosure Recommendations in Statement of Position

<i>SOP Par.</i>	<i>Nature of Disclosure</i>
.21	Accounting policy—methods of reporting revenue
.45	Method or methods of measuring extent of progress toward completion
.52	Criteria for determining substantial completion
.65–.67	Information on revenue and costs arising from claims
.84	Effects of changes in estimates on contracts
.90–.91	Effects of accounting changes to conform to SOP

Appendix D

Schedule of Changes Made to Statement of Position 81-1, Accounting for Performance of Construction-Type and Certain Production-Type Contracts

<u>Reference</u>	<u>Change</u>	<u>Date</u>
General	Deleted "Audits of" in all references to all applicable Guide titles.	May, 2004
Appendix title	Footnote * added.	May, 2002
Notice to Readers	Revised to reflect the issuance of SAS No. 69.	June, 1998
Paragraph .03	Note reference to supersession of APB Statement No. 4 added.	May, 1993
Paragraph .04	Reference to Industry Audit Guide <i>Audits of Government Contractors</i> , deleted.	October, 1990
Paragraph .14	Footnote deleted.	October, 1990
Paragraphs .18 and .19	References to Industry Audit Guide <i>Audits of Government Contractors</i> , have been changed to Audit and Accounting Guide <i>Audits of Federal Government Contractors</i> .	October, 1990
Paragraph .38	Footnote deleted.	October, 1990
Paragraph .72	References in footnotes 11 and 13 to Industry Audit Guide <i>Audits of Government Contractors</i> , have been changed to Audit and Accounting Guide <i>Audits of Federal Government Contractors</i> .	October, 1990
Paragraph .75	Footnote deleted.	October, 1990
Paragraph .75(a)	Footnote added to reflect the issuance of SOP 98-5.	June, 1998
Paragraphs .83, .84, .90, and .91	Revised to reflect the issuance of FASB Statement No. 154.	June, 2007
Appendix B	References in footnotes 1 and 2 to Industry Audit Guide <i>Audits of Government Contractors</i> , have been changed to Audit and Accounting Guide <i>Audits of Federal Government Contractors</i> .	October, 1990
Appendix B	References in footnotes 1 and 2 delete Guide section numbers and, in their place, insert Guide section titles.	May, 2003

ACCOUNTING STANDARDS DIVISION

Accounting Standards Executive Committee (1979—1980)

DENNIS R. BERESFORD, *Chairman*
MICHAEL P. BOHAN
ROGER CASON
JOEL W. CHEMERS
ROBERT HAMPTON III
GERALD W. HEPP
JOHN W. HOYT
C. FOSTER JENNINGS

MITCHELL M. KRASNOFF
WILLIAM D. MAHANEY
PAUL E. NORD
THOMAS J. O'REILLY
JOHN J. ROBBINS
WALTER SCHUETZE
JERRY J. WEYGANDT

Construction Contractor Guide Committee

RICHARD S. HICKOK, *Chairman*
WILLIAM J. PALMER, *Vice Chairman*
EUGENE S. ABERNATHY
DENNIS W. BERSCH
DONALD L. BRENNER
JAMES A. DOWSLEY
BERNARD D. DUSENBERRY
ELI HOFFMAN
PETER A. HOFFMAN

FRANCIS E. KASTENHOLZ
JAMES J. LEISENRING
JOSEPH J. MORDINI,
Member through 1977-78
MARK A. PINEDO
CHARLES L. ROBERTSON
MELVIN ROSENSTRAUCH
ERNEST G. WEBER

AICPA Staff

PAUL ROSENFELD, *Director*
Accounting Standards
STEVE RUBIN, *Manager*
Accounting Standards

THOMAS W. MCRAE, *Manager*
Accounting Standards

[The next page is 18,931.]

Section 10,330**Statement of Position 81-1*
Accounting for Performance of
Construction-Type and Certain
Production-Type Contracts**

July 15, 1981

[Proposal to the Financial Accounting Standards Board]

Note: Statement of Position 81-1, *Accounting for Performance of Construction-Type and Certain Production-Type Contracts*, has been modified by the AICPA staff to include certain changes necessary due to the issuance of authoritative pronouncements since it was originally issued. The changes are identified in a schedule in Appendix D of the statement.

NOTE

Statements of Position of the Accounting Standards Division present the conclusions of at least a majority of the Accounting Standards Executive Committee, which is the senior technical body of the AICPA authorized to speak for the Institute in the areas of financial accounting and reporting. Statement on Auditing Standards No. 69, *The Meaning of Present Fairly in Conformity With Generally Accepted Accounting Principles*, identifies AICPA Statements of Position as sources of established accounting principles that an AICPA member should consider if the accounting treatment of a transaction or event is not specified by a pronouncement covered by Rule 203 of the AICPA Code of Professional Conduct. In such circumstances, the accounting treatment specified by this Statement of Position should be used or the member should be prepared to justify a conclusion that another treatment better presents the substance of the transaction in the circumstances. However, an entity need not change an accounting treatment followed as of March 15, 1992 to the accounting treatment specified in this Statement of Position.

Introduction

.01 This statement of position provides guidance on the application of generally accepted accounting principles in accounting for the performance of contracts for which specifications are provided by the customer for the construction of facilities or the production of goods or for the provision of related services. Changes in the business environment have increased significantly the variety and uses of those types of contracts and the types of business enterprises that use them. In the present business environment, diverse types of contracts, ranging from relatively simple to highly complex and from relatively short- to long-term, are widely used in many industries for construction, production, or provision of a broad range of goods and services. However, existing principles related to accounting for contracts were written in terms of long-term construction-type contracts, and they are not stated in sufficient detail for the scope of activities

* Transactions within the scope of SOP 81-1 are not subject to the views expressed in Staff Accounting Bulletin (SAB) 101, *Revenue Recognition in Financial Statements*, issued by the Securities and Exchange Commission.
